



# Regional Freeway and Highway Program Construction Update

Brent Cain, PE. Deputy State Engineer  
February 19, 2014






# Projects Under Construction

- 24 Projects Under Construction
  - 5 State Funded Projects
  - 19 Federally Funded Projects
    - 10 LPA Projects (Local Public Agency)
  
- Overall Contract Cost - \$ 366 Million

January 2013 Certification

# Regional Transportation Plan Freeway Program Phases I - IV, 2006 - 2025

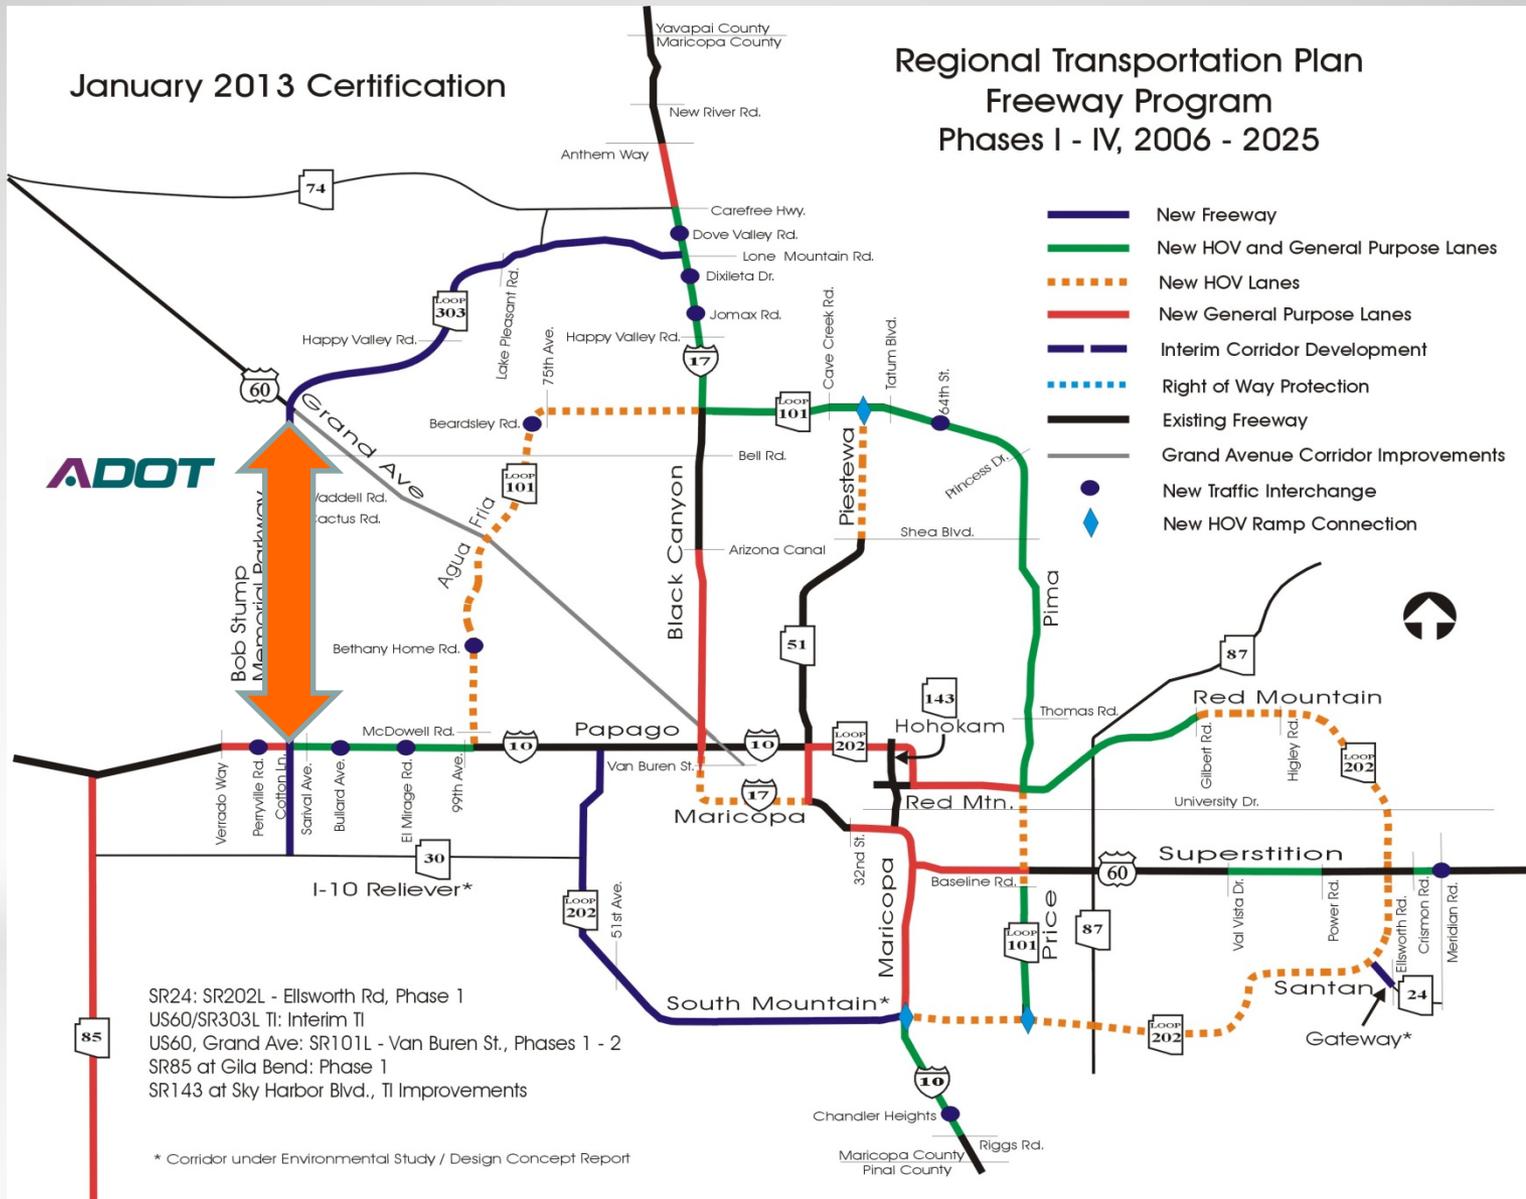

# L303 Projects

<b>L303 Segments</b>	<b>Projects</b>	<b>Length</b>	<b>Construction Cost</b>
Segment 1	I-10 / L303 TI	1.3 Miles	\$ 158,147,019.00
Segment 2	L303, Thomas Rd. - Camelback Rd.	2 Miles	\$ 37,729,965.00
Segment 3	L303, Camelback Rd. - Glendale Ave.	2 Miles	\$ 50,033,800.00
Segment 4	L303, Glendale Ave. - Peoria Ave.	3 Miles	\$ 78,984,874.00
Segment 5 - CMAR Project	L303, Peoria Ave. - Mountain View Rd.	6 Miles	\$ 148,065,806.18
			<b>\$ 472,961,464.18</b>

## Project: I-10 / SR 303 TI

Contractor: Pulice Construction, Inc.

Construction Cost: \$158 Million



Construction Start Date: November 2011

The Project is 94% complete.

Estimated Completion – Early Fall-2014



**Project: L303, Thomas Rd. to Camelback Rd.**

Contractor: Ames Construction, Inc.

Construction Cost: \$38 Million



Construction Start Date: July, 2012

Project is Substantially Complete as of November-2013

## Project: L303, Camelback Rd. to Glendale Ave.

Contractor: Pulice Construction, Inc.

Construction Cost: \$50 Million



Construction Start Date: March, 2013

The Project is 70% complete.

Estimated Completion – Late Summer-2014



**Project: L303, Glendale Ave. to Peoria Ave.**

Contractor: Pulice Construction, Inc.

Construction Cost: \$79 Million



Construction Start Date: May, 2012

Project is Substantially Complete as of February-2014



# CMAR Project: L303, Peoria Ave. to Mountain View Blvd.

Contractor: Pulice Construction, Inc.

Construction Cost: \$148 Million



Construction Start Date: August, 2011

Project is Substantially Complete as of November-2013






# L303 Landscaping Projects

- ✓ Waddell Rd. to Mountain View Blvd. (Under Construction)
- ✓ Peoria Ave. to Waddell Rd. (Under Construction)
- ✓ Glendale Ave. to Peoria Ave. (Advertisement – June 2014)
- ✓ Camelback Rd. - Glendale Ave. (Advertisement – July 2014)
- ✓ Thomas Rd. - Camelback Rd. (Advertisement – July 2014)
- ✓ L303 / I-10 TI (Advertisement – FY 2015)

January 2013 Certification

# Regional Transportation Plan Freeway Program Phases I - IV, 2006 - 2025

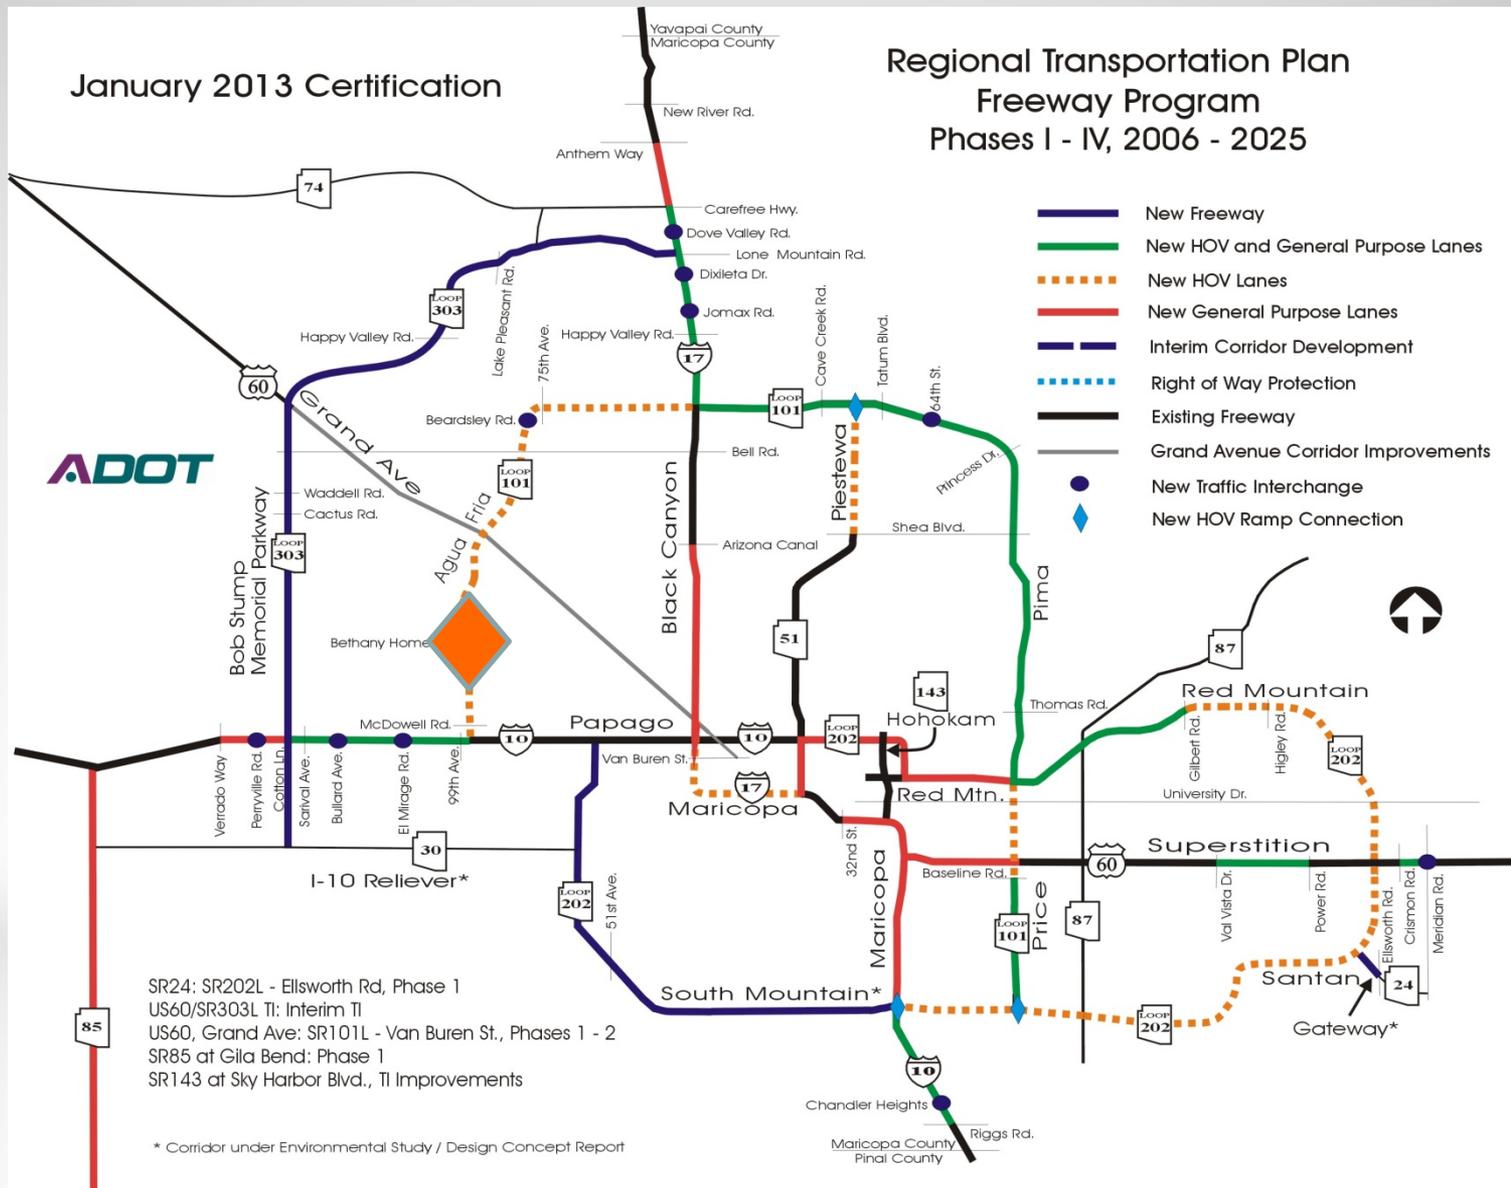

SR24: SR202L - Ellsworth Rd, Phase 1  
 US60/SR303L TI: Interim TI  
 US60, Grand Ave: SR101L - Van Buren St., Phases 1 - 2  
 SR85 at Gila Bend: Phase 1  
 SR143 at Sky Harbor Blvd., TI Improvements

\* Corridor under Environmental Study / Design Concept Report



# L101, Maryland Ave. DHOV Ramps Design Build Project

Design Builder: Coffman Specialties, Inc. – TY-Lin

Construction Cost: \$13 Million



Construction Start Date: September, 2013


The Project is 71% complete.

Estimated Completion – April-2014



January 2013 Certification

# Regional Transportation Plan Freeway Program Phases I - IV, 2006 - 2025

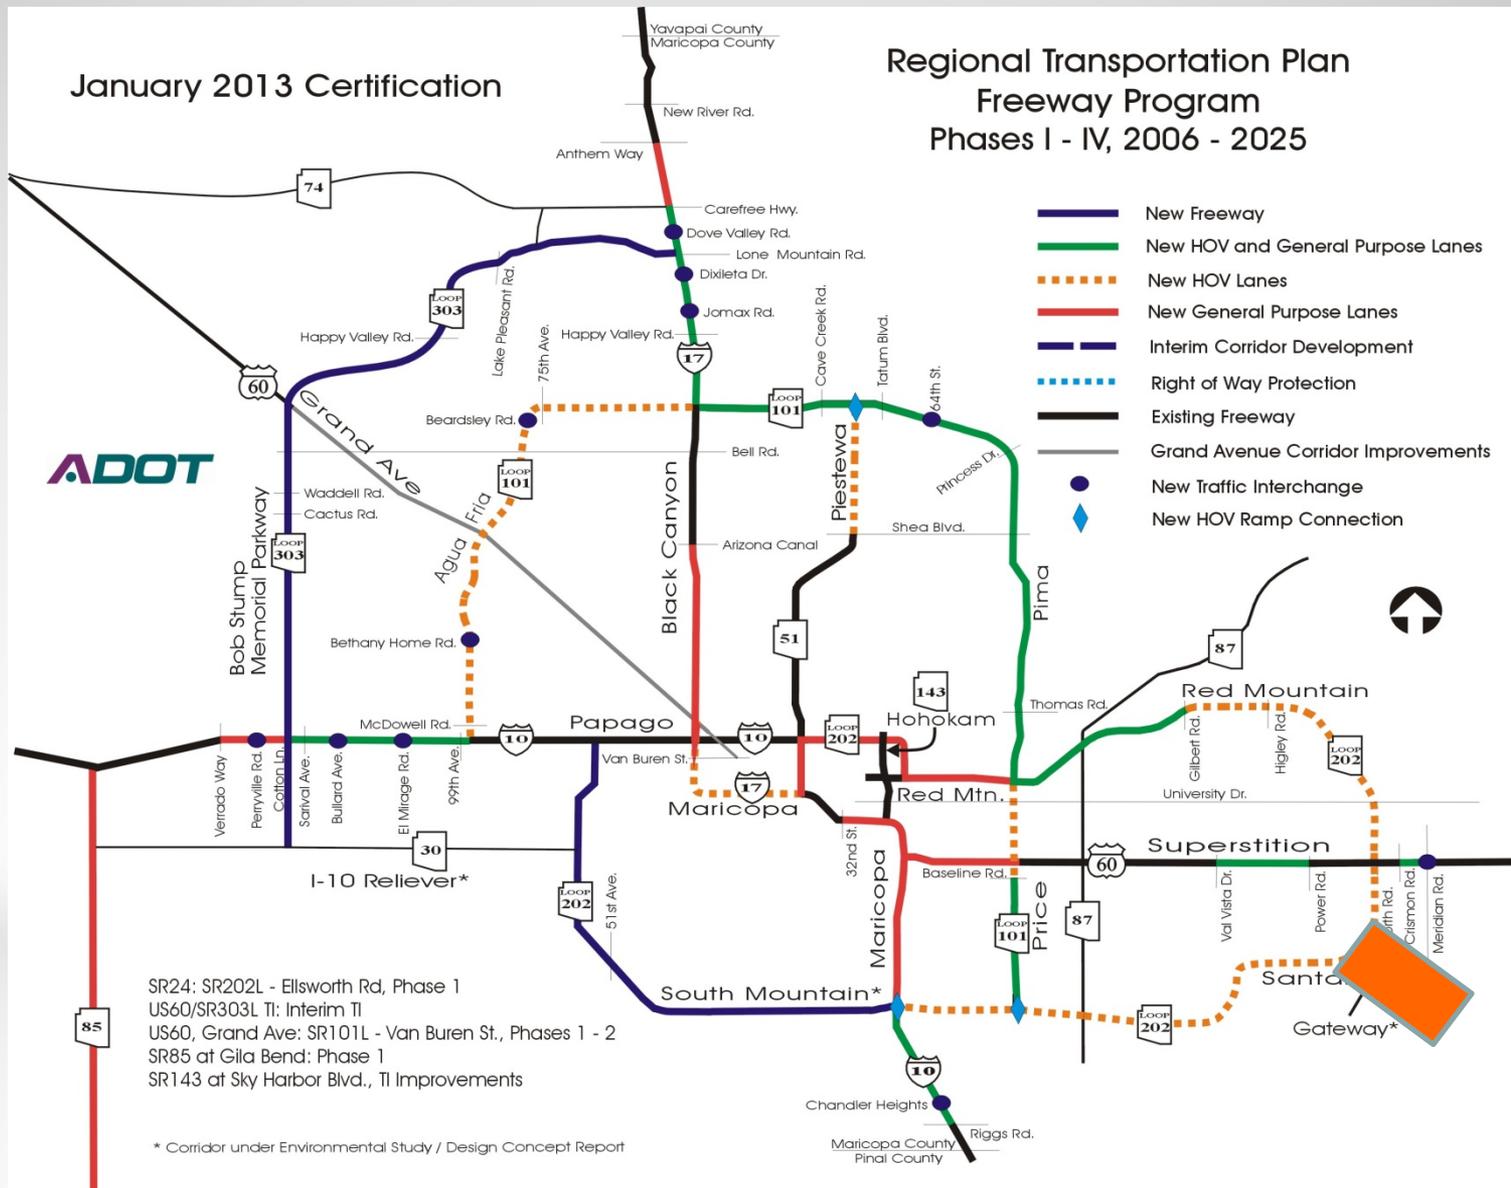

SR24: SR202L - Ellsworth Rd, Phase 1  
 US60/SR303L TI: Interim TI  
 US60, Grand Ave: SR101L - Van Buren St., Phases 1 - 2  
 SR85 at Gila Bend: Phase 1  
 SR143 at Sky Harbor Blvd., TI Improvements

\* Corridor under Environmental Study / Design Concept Report

## SR 24 (Gateway Freeway)

Contractor: Ralph L. Wadsworth Construction Company

Construction Cost: \$82 Million



Construction Start Date: March, 2012


The Project is 95% complete.

Estimated Completion – Late Spring-2014



January 2013 Certification

# Regional Transportation Plan Freeway Program Phases I - IV, 2006 - 2025

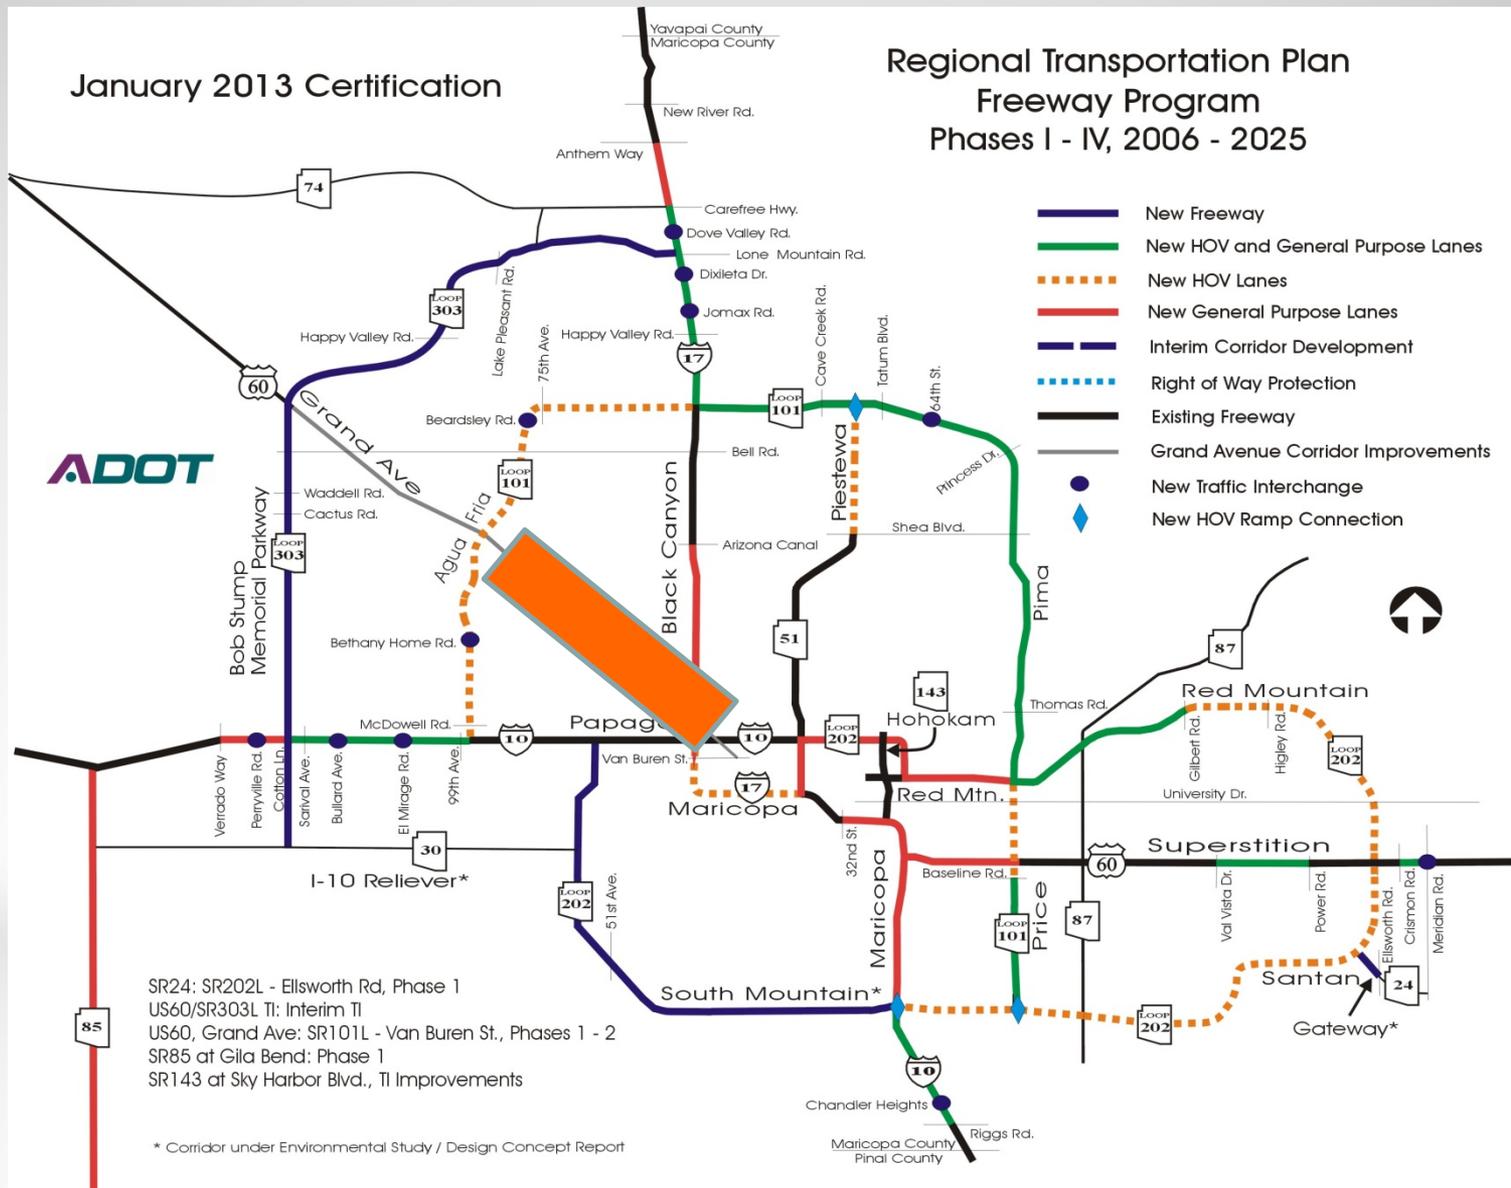

## US 60 (Grand Avenue) – 19<sup>th</sup> Ave. to 71<sup>st</sup> Ave.

Contractor: Nesbitt Contracting Co., Inc.

Construction Cost: \$18 Million



Construction Start Date: January, 2013

The Project is 70% complete.

Estimated Completion – Late Spring-2014



# Upcoming 2014 Projects

January 2013 Certification

# Regional Transportation Plan Freeway Program Phases I - IV, 2006 - 2025

**L303, El Mirage Rd. TI**

**L303 DB, US 60 - HVP**


**SR 51, Black Mtn. Blvd.**

**L101, L202 – Shea Blvd.**

**L202 DB, L101 –  
Broadway Rd.**

**L303 / US 60 TI CMAR**

**Meridian Rd. TI**

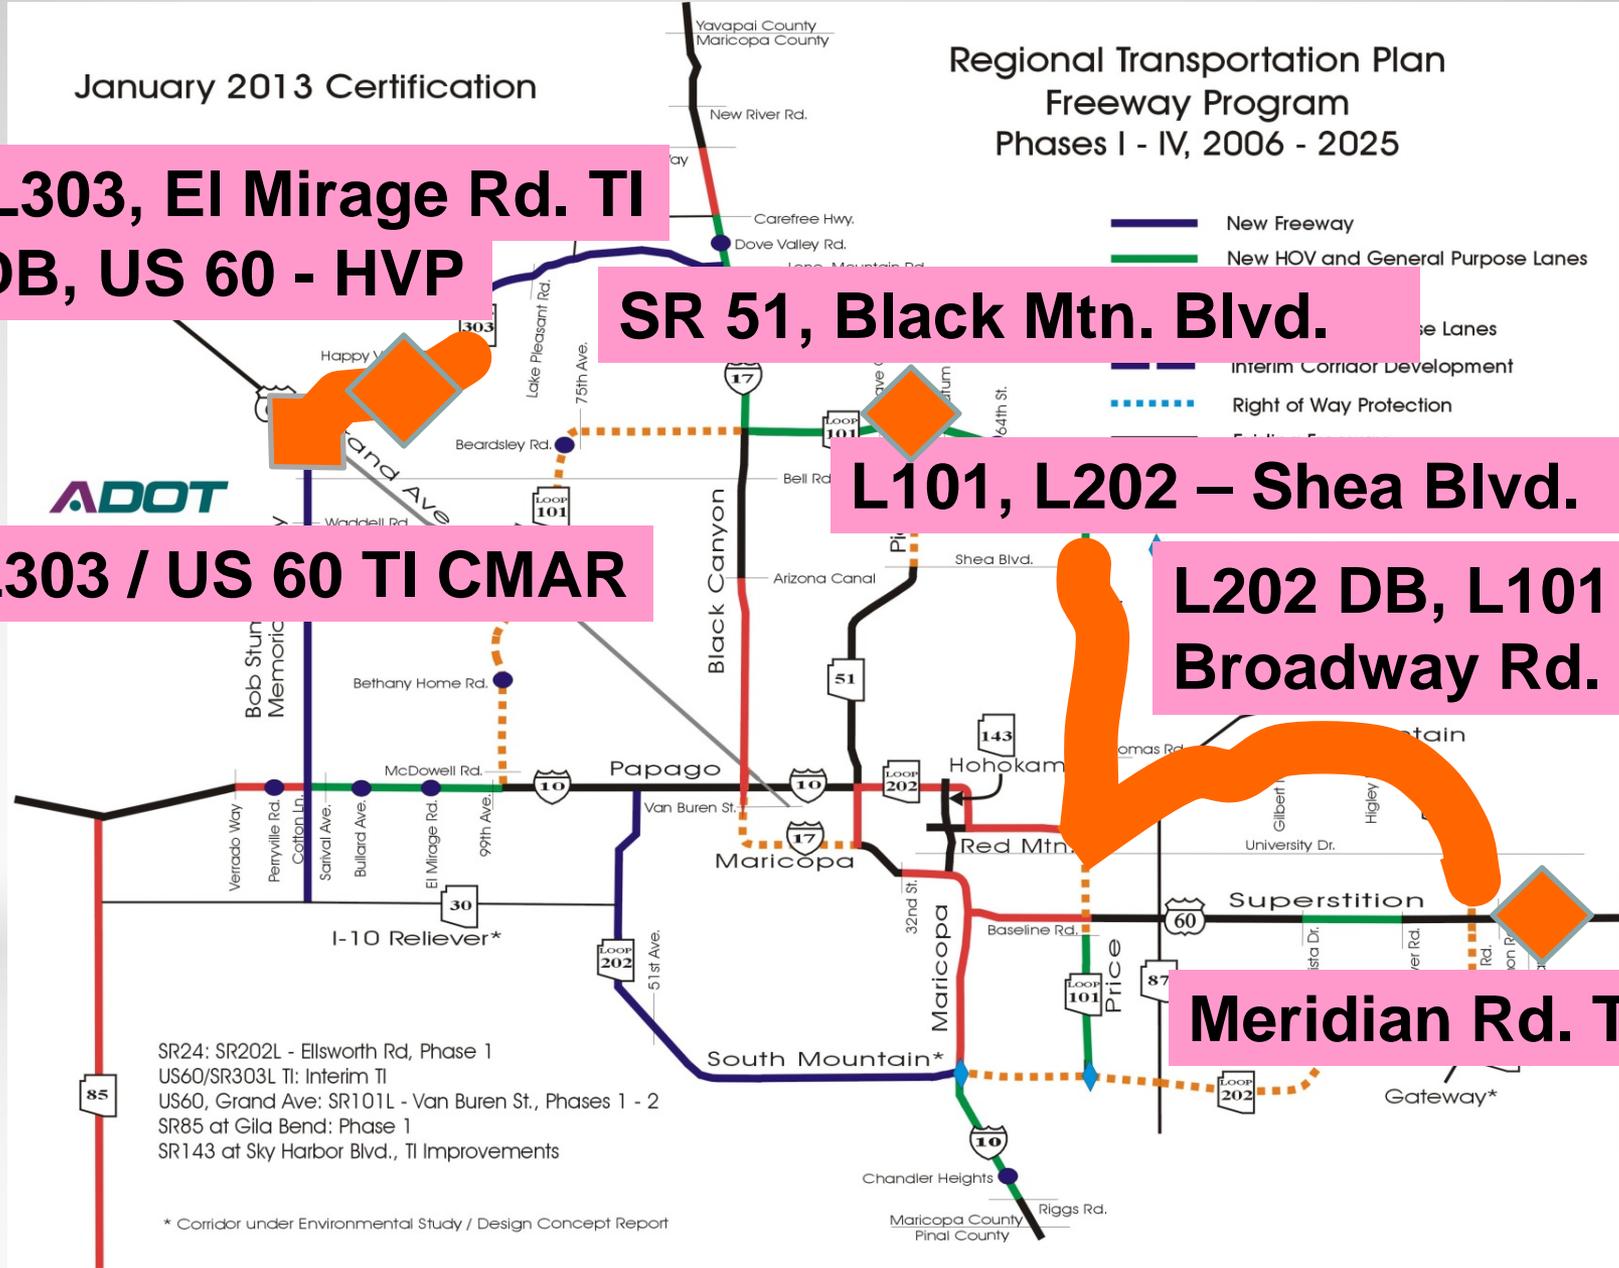

SR24: SR202L - Ellsworth Rd, Phase 1  
 US60/SR303L TI: Interim TI  
 US60, Grand Ave: SR101L - Van Buren St., Phases 1 - 2  
 SR85 at Gila Bend: Phase 1  
 SR143 at Sky Harbor Blvd., TI Improvements

\* Corridor under Environmental Study / Design Concept Report

# Upcoming 2014 Projects

## East Valley

- ✓ SR101, L202 – Shea Blvd. GP Lanes – Advertise April, 2014
- ✓ SR202, L101 – Broadway Rd. GP and HOV Lanes Design Build - Award August 2014
- ✓ US60, Meridian Rd. Half Diamond TI – Advertise June, 2014
- ✓ SR51, Black Mountain Blvd. TI CMAR – Award May 2014

## West Valley

- ✓ SR303, US 60/SR 303 TI CMAR – Award July 2014
- ✓ SR303, US 60 – Happy Valley Rd. Design Build – Award June, 2014
- ✓ SR303, El Mirage TI – Advertise June 2014

# Regional Freeway and Highway Program Construction Update



Brent Cain, PE.  
Deputy State Engineer, Urban Operations  
BCain@azdot.gov  
602-712-8274
