



# Proposition 400


## ALCP STATUS REPORT

### FY2026 January – June 2026



# OVERVIEW

The Arterial Street Life Cycle Program (ALCP) is maintained by the Maricopa Association of Governments (MAG) and implements arterial street projects funded as part of the Proposition 400 program. The ALCP provides regional funding to widen existing streets, improve intersections, and construct new arterial segments. The program also provides information on MAG planning studies and project implementation of the regional arterial Intelligent Transportation System (ITS) Plan funded in the program.

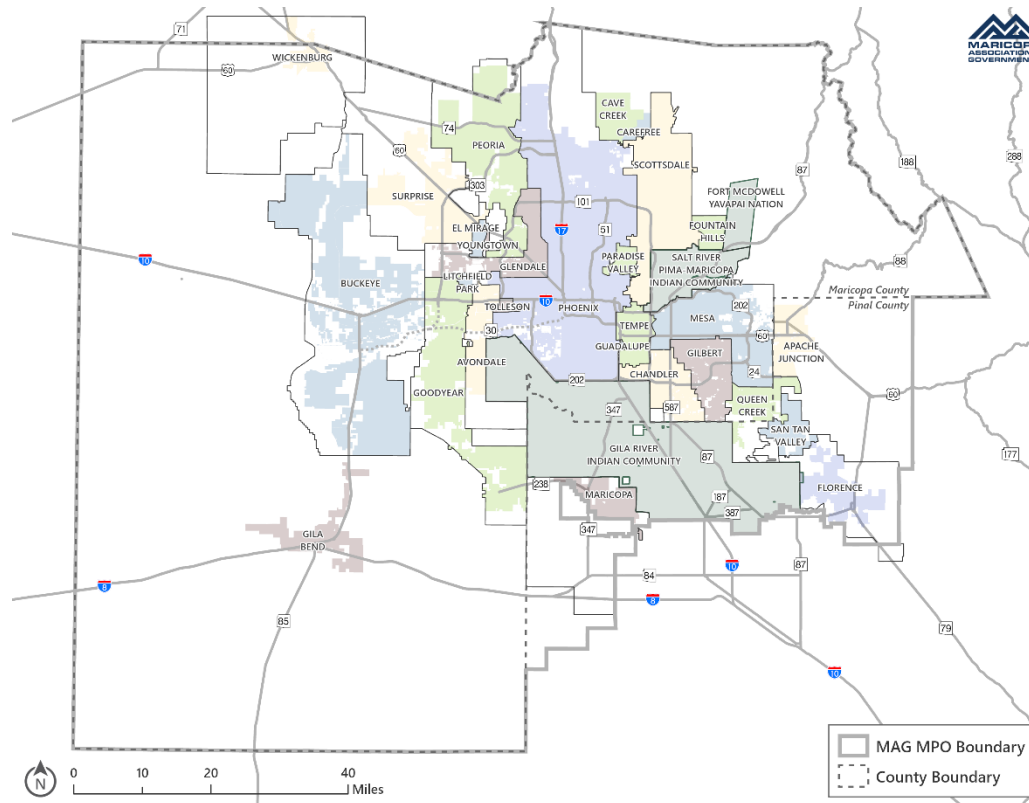

## ALCP Revenue and Finance

In November 2004, the voters of Maricopa County approved Proposition 400, which extended the half cent sales tax for transportation through 2025. The tax extension was divided among freeways (56.2 percent), transit (33.3 percent) and arterial streets (10.5 percent). The portion of the tax extension allocated is managed through the ALCP and deposited into the Regional Area Road Fund (RARF) arterial account on a monthly basis. Proposition 400 collections ended on December 31, 2025. A breakdown of revenues by mode collected from July 2025 to June 2026 for the current fiscal year is provided in Table 1.

**TABLE 1: FISCAL YEAR 2026 PROPOSITION 400 COLLECTIONS (JULY 2025 – JUNE 2026)**

|              | Freeways             | Arterial Streets    | Transit              | Total                | Estimate             | % Difference |
|--------------|----------------------|---------------------|----------------------|----------------------|----------------------|--------------|
| July         | \$36,882,150         | \$6,890,793         | \$21,853,658         | \$65,626,602         | \$65,610,000         | 0.03%        |
| August       | \$35,118,519         | \$6,561,289         | \$20,808,660         | \$62,488,469         | \$61,790,000         | 1.13%        |
| September    | \$35,275,575         | \$6,590,632         | \$20,901,720         | \$62,767,928         | \$61,680,000         | 1.76%        |
| October      | \$36,105,435         | \$6,745,677         | \$21,393,434         | \$64,244,547         | \$63,980,000         | 0.41%        |
| November     | \$37,337,765         | \$6,975,917         | \$22,123,623         | \$66,437,305         | \$64,480,000         | 3.07%        |
| December     | \$36,118,787         | \$6,748,172         | \$21,401,346         | \$64,268,305         | \$64,400,000         | (0.20%)      |
| January      | \$43,560,662         | \$8,138,551         | \$25,810,835         | \$77,540,641         | \$75,580,000         | 2.58%        |
| February     | \$1,838,654          | \$343,513           | \$1,089,428          | \$3,271,596          | \$0                  | -            |
| March        | \$686,014            | \$128,169           | \$406,477            | \$1,220,660          | \$0                  | -            |
| April        | -\$240,565           | -\$44,948           | -\$142,549           | -\$428,061           | \$0                  | -            |
| May          | \$533,883            | \$99,747            | \$316,340            | \$949,969            | \$0                  | -            |
| June         | -                    | -                   | -                    | -                    | \$0                  | -            |
| <b>TOTAL</b> | <b>\$263,217,660</b> | <b>\$49,177,514</b> | <b>\$155,962,972</b> | <b>\$468,358,146</b> | <b>\$457,520,000</b> | <b>2.37%</b> |

In addition to the half-cent sales tax, the Regional Transportation Plan (RTP) sets aside a portion of federal Surface Transportation Block Grant Program (STBGP) and Congestion Mitigation and Air Quality Improvement Program (CMAQ) funds allocated to the region to fund projects in the ALCP.

Revenues from the half cent sales tax allocated to arterials are deposited into the Regional Area Road Fund (RARF) arterial account on a monthly basis. Fiscal Year (FY) 2026 RARF revenues were 2.4% percent higher than the September 2025 Arizona Department of Transportation (ADOT) forecast. Table 2 provides a summary of estimated versus actual arterial RARF revenue collections.

Since the initiation of the tax in January 2006 through December 2025, approximately \$987.5 million in RARF revenues have been collected for arterial improvements in the region, \$40.3 million has been earned through income from investments, and more than \$739.4 million of project expenses have been reimbursed. At the end of June 2026, the RARF project account balance was \$275.35 million.

The RTP dedicates approximately 3.65 percent of the ALCP RARF funds for planning and implementation studies in the region. The funding allocated for implementation studies is contingent on RARF revenue collections. As a result, the amounts programmed in the ALCP are estimates derived from the annual ADOT RARF revenue forecasts. The remaining regional budget for the implementation studies fluctuates concurrently with the forecasts. Since 2006, \$34.3 million in RARF revenues have been deposited into the RARF Studies account.

**TABLE 2: FISCAL YEAR 2026 TOTAL ARTERIAL RARF COLLECTIONS**

|              | Estimated total RARF | Actual RARF*        | Percentage Difference |
|--------------|----------------------|---------------------|-----------------------|
| July         | \$6,889,050          | \$6,890,793         | 0.03%                 |
| August       | \$6,487,950          | \$6,561,289         | 1.13%                 |
| September    | \$6,476,400          | \$6,590,632         | 1.76%                 |
| October      | \$6,717,900          | \$6,745,677         | 0.41%                 |
| November     | \$6,770,400          | \$6,975,917         | 3.04%                 |
| December     | \$6,762,000          | \$6,748,172         | (0.20%)               |
| January      | \$7,935,900          | \$8,138,551         | 2.55%                 |
| February     | \$0                  | \$343,513           | -                     |
| March        | \$0                  | \$128,169           | -                     |
| April        | \$0                  | -\$44,948           | -                     |
| May          | \$0                  | \$99,747            | -                     |
| June         | \$0                  | -                   | -                     |
| <b>TOTAL</b> | <b>\$48,039,600</b>  | <b>\$49,177,514</b> | <b>2.4%</b>           |

## Project Highlight

### VAL VISTA DRIVE: THE U.S 60 TO PUEBLO AVENUE

The City of Mesa is currently reconstructing Val Vista Drive from the U.S 60 to Pueblo Avenue. Planned Improvements include widening Val Vista Drive to three lanes, rebuilding new roadway pavement, adding bike lanes, raised center medians, drainage improvements and traffic signal modifications. Construction began in August 2025 and is estimated to be completed in Spring 2027.

For additional information, please contact the City of Mesa at 480-644-3800.

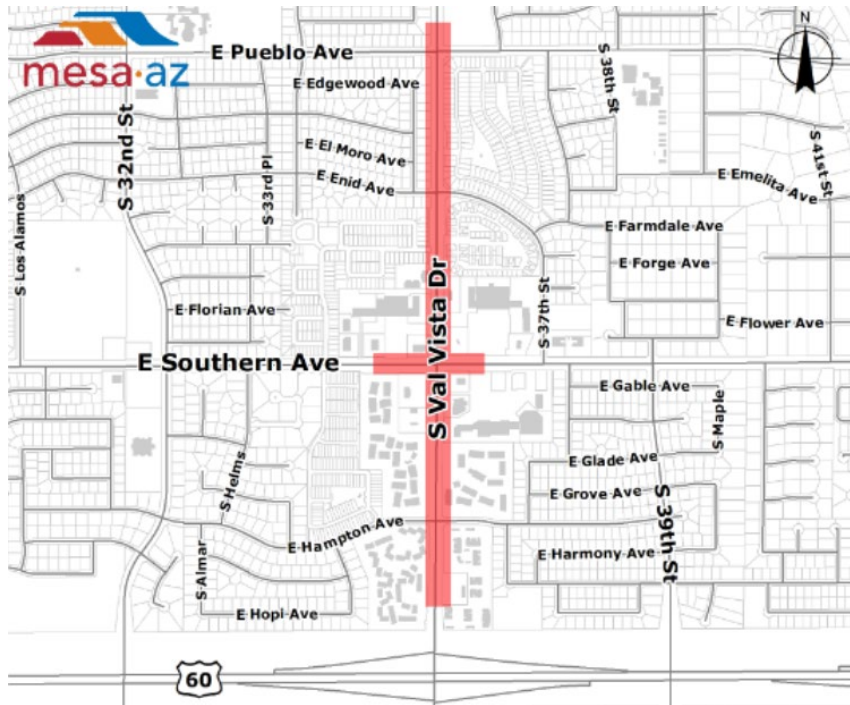


Photo provided by the [City of Mesa](#)

# FY 2026 Arterial Life Cycle Program

On June 25, 2025, the MAG Regional Council approved the FY 2026 Arterial Life Cycle Program and amendments to the MAG FY 2025-2030 Transportation Improvement Program.

An electronic copy of the [FY 2026 ALCP](#) may be downloaded from the MAG website.

## ALCP Project Status

Detailed information about projects underway is provided in Tables 3, 4.1 and 4.2. Table 3 includes all projects programmed for work and/or reimbursement in FY 2026, the amount programmed for reimbursement in FY 2026, and ALCP project requirements submitted to-date. Tables 4.1 and 4.2 detail project reimbursements and expenditures for projects programmed for work and/or reimbursement in FY 2026.

This is the 43rd Status Report for the ALCP. Semi-annually, MAG provides member agencies with an update on the projects in the ALCP. This report and all other ALCP information are available online at: <https://azmag.gov/Programs/Transportation/Arterial-Life-Cycle-Program/Proposition-400-Arterial-Life-Cycle-Program>.

**Table 3: Fiscal Year (FY) 2026 Schedule of projects programmed for work/reimbursement in FY 2026**

| Facility/Location                               | RTP ID          | FY 26 Programming      | FY 26 Work Phase | FY 26 Programmed Reimbursement | FY Reimbursed through 6/30/2026 | Project Overview (PO) | Project Agreement (PA) | Needed in FY 26 |
|-------------------------------------------------|-----------------|------------------------|------------------|--------------------------------|---------------------------------|-----------------------|------------------------|-----------------|
| <b>CHANDLER</b>                                 |                 |                        |                  |                                |                                 |                       |                        |                 |
| Chandler Heights Rd: Gilbert Rd to Val Vista Rd | ACI-PRC-10-03-K | Work and Reimbursement | Construction     | Funds obligated in FFY 24      | 8,899,108.96                    | Completed 7/2021      | Completed 11/2021      | ---             |
| Ocotillo Rd: Gilbert Rd to 148th St             | ACI-OCT-10-03   | Work and Reimbursement | Construction     | Funds obligated in FFYs 16/21  | -                               | Completed 8/2016      | Completed 10/2016      | ---             |
| Lindsay Road: Ocotillo Rd to Hunt Hwy           | ACI-LND-10-03   | Work and Reimbursement | Construction     | Funds obligated in FFY 25      | 1,086,178.91                    | Completed 7/2020      | Completed 8/2020       | PRR             |
| <b>FOUNTAIN HILLS</b>                           |                 |                        |                  |                                |                                 |                       |                        |                 |
| Shea Blvd: Palisades Blvd to Technology Dr      | ACI-SHA-10-03-C | Work and Reimbursement | Construction     | 2,280,817.21                   | 590,992.22                      | Completed 1/2021      | Completed 3/2021       | PRR             |

| Facility/Location                                                           | RTP ID          | FY 26 Programming      | FY 26 Work Phase | FY 26 Programmed Reimbursement   | FY Reimbursed through 6/30/2026 | Project Overview (PO) | Project Agreement (PA) | Needed in FY 26 |
|-----------------------------------------------------------------------------|-----------------|------------------------|------------------|----------------------------------|---------------------------------|-----------------------|------------------------|-----------------|
| <b>GILBERT</b>                                                              |                 |                        |                  |                                  |                                 |                       |                        |                 |
| Elliot Rd at Cooper Rd: Intersection Improvements                           | AII-ELT-30-03   | Reimbursement Only     | N/A              | 4,328,803.21                     | -                               | Completed 8/2014      | Completed 5/2015       | PRR             |
| McQueen Rd at Elliot Rd                                                     | AII-MCQ-30-03   | Reimbursement Only     | N/A              | 6,324,333.16                     | 1,187,336.20                    | Completed 9/2024      | Completed 10/2024      | PRR             |
| McQueen Rd at Guadalupe Rd                                                  | AII-MCQ-40-03   | Reimbursement Only     | N/A              | 6,844,346.18                     | -                               | Completed 6/2026      | ---                    | PA/PRR          |
| Warner Rd: Recker Rd to Power Rd                                            | ACI-WRN-20-03   | Reimbursement Only     | N/A              | 10,416,851.61                    | -                               | Completed 1/2022      | Completed 7/2022       | PRR             |
| <b>GILBERT/MARICOPA COUNTY/MESA/QUEEN CREEK</b>                             |                 |                        |                  |                                  |                                 |                       |                        |                 |
| Power Rd: East Maricopa Floodway to Santan Fwy/Loop 202 (Pre-design) - Mesa | ACI-PWR-20-03-A | Work and Reimbursement | Construction     | 7,741,971.54                     | 376,788.79                      | Completed 11/2024     | Completed 12/2024      | PRR             |
| <b>MARICOPA COUNTY</b>                                                      |                 |                        |                  |                                  |                                 |                       |                        |                 |
| Gilbert Rd: Bridge over the Salt River                                      | ACI-GIL-20-03   | Reimbursement Only     | N/A              | 2,531,805.96                     | 867,379.85                      | Completed 3/2016      | Completed 5/2016       | ---             |
| McKellips Rd: Loop 101 to SRP-MIC/Alma School Rd                            | ACI-MCK-40-03   | Reimbursement Only     | N/A              | 9,452,806.80                     | 9,452,806.80                    | Completed 9/2016      | Completed 3/2017       | PRR             |
| Main St: Sossaman Rd to Meridian Rd (ADOT Administered)                     | ACI-MAN-10-03   | Work and Reimbursement | Construction     | Funds obligated in FFY 23        | -                               | Completed 6/2022      | ---                    | ---             |
| Northern Parkway: Dysart to 111th Ave                                       | ACI-NOR-10-03-B | Reimbursement Only     | N/A              | Funds obligated in FFYs 12/14/18 | -                               | Completed 6/2012      | Completed 11/2012      | ---             |
| Northern Parkway: 103rd to 91st Ave                                         | ACI-NOR-10-03-D | Work and Reimbursement | Construction     | 46,019,811.42                    | 1,337,240.68                    | Completed 11/2012     | Completed 1/2013       | PRR             |
| Northern Parkway: SR 101 RBCB Extension                                     | ACI-NOR-10-03-J | Work and Reimbursement | Construction     | Funds obligated in FFY 24        | 156,311.17                      | Completed 7/2024      | Completed 12/2024      | PRR             |
| Northern Parkway: El Mirage Alternative Access                              | ACI-NOR-20-03-A | Work and Reimbursement | Construction     | Funds obligated in FFYs 19/21/22 | -                               | Completed 4/2018      | Completed 8/2021       | ---             |

| Facility/Location                                            | RTP ID          | FY 26 Programming      | FY 26 Work Phase | FY 26 Programmed Reimbursement | FY Reimbursed through 6/30/2026 | Project Overview (PO) | Project Agreement (PA) | Needed in FY 26 |
|--------------------------------------------------------------|-----------------|------------------------|------------------|--------------------------------|---------------------------------|-----------------------|------------------------|-----------------|
| <b>MARICOPA COUNTY (Cont.)</b>                               |                 |                        |                  |                                |                                 |                       |                        |                 |
| Northern Parkway: Agua Fria to 103th Ave                     | ACI-NOR-20-03-C | Work and Reimbursement | Construction     | Funds obligated in FFY 25      | 161,208.91                      | Completed 4/2022      | Completed 5/2022       | PRR             |
| <b>MESA</b>                                                  |                 |                        |                  |                                |                                 |                       |                        |                 |
| Broadway Rd: Country Club Dr to Mesa Dr                      | ACI-BDW-20-03-A | Work and Reimbursement | Right of Way     | 1,091,493.07                   | -                               | ---                   | ---                    | PO/PA/PRR       |
| Broadway Rd: Mesa Dr to Stapley Dr                           | ACI-BDW-20-03-B | Work and Reimbursement | Construction     | 45,300,403.15                  | 1,305,310.46                    | Completed 2/2019      | Completed 5/2019       | PRR             |
| Country Club Dr: US 60 to Southern Ave                       | ACI-CCB-20-03   | Work and Reimbursement | Construction     | 7,985,678.40                   | -                               | Completed 6/2026      | ---                    | PA/PRR          |
| Elliot Road: Eastern Maricopa Floodway (EMF) to Ellsworth Rd | ACI-ELT-10-03-F | Reimbursement Only     | N/A              | 22,510,064.25                  | 758,065.66                      | Completed 7/2022      | Completed 10/2022      | PRR             |
| Mesa Dr: US 60 to Southern Ave                               | ACI-MES-10-03-A | Reimbursement Only     | N/A              | 36,384.70                      | -                               | Completed 3/2007      | Completed 1/2008       | ---             |
| Mesa Dr: 8th Ave to Main St                                  | ACI-MES-10-03-B | Reimbursement Only     | N/A              | 527,056.41                     | -                               | Completed 6/2014      | Completed 8/2014       | ---             |
| SR-24 Arterial Improvements                                  | ACI-ELL-10-03-A | Reimbursement Only     | N/A              | 810,622.23                     | -                               | ---                   | ---                    | Savings         |
| Signal Butte Rd: Williams Field Rd to Germann Rd             | ACI-SGB-10-03-C | Reimbursement Only     | N/A              | 3,171,006.60                   | -                               | Completed 6/2019      | Completed 8/2019       | Savings         |
| Southern Ave at Stapley Dr: Intersection Improvements        | ACI-SOU-10-03-B | Reimbursement Only     | N/A              | 1,296,187.26                   | -                               | Completed 8/2017      | Completed 10/2017      | Savings         |
| Stapley Dr at University Dr: Intersection Improvements       | ACI-STA-10-03   | Reimbursement Only     | N/A              | 1,551,657.67                   | -                               | Completed 11/2021     | Completed 2/2022       | PRR             |
| Val Vista Dr: US 60 to Pueblo                                | ACI-VAL-10-03-C | Work and Reimbursement | Construction     | 12,027,092.34                  | 1,584,213.32                    | Completed 4/2021      | Completed 5/2021       | PRR             |
| Ray Road: SR 24 to Ellsworth Rd                              | ACI-RAY-30-03   | Work and Reimbursement | Construction     | 8,008,717.56                   | 4,778,073.23                    | Completed 9/2022      | Completed 11/2020      | PRR             |

| Facility/Location                                            | RTP ID          | FY 26<br>Programming   | FY 26 Work<br>Phase | FY 26 Programmed<br>Reimbursement | FY Reimbursed<br>through 6/30/2026 | Project<br>Overview<br>(PO) | Project<br>Agreement<br>(PA) | Needed in<br>FY 26 |
|--------------------------------------------------------------|-----------------|------------------------|---------------------|-----------------------------------|------------------------------------|-----------------------------|------------------------------|--------------------|
| <b>MESA (Cont.)</b>                                          |                 |                        |                     |                                   |                                    |                             |                              |                    |
| Ellsworth Rd and Williams Field Rd Bridge                    | ACI-ELL-20-03-A | Work and Reimbursement | Construction        | 1,064,181.93                      | -                                  | Completed 4/2021            | Completed 5/2021             | PRR                |
| Ellsworth Rd: Germann to Ray Rd                              | ACI-ELL-20-03-B | Work and Reimbursement | Right of Way        | 23,946,395.05                     | 2,971,907.01                       | Completed 7/2022            | Completed 10/2022            | PRR                |
| Williams Field Rd: SR24 to Ellsworth                         | ACI-ELL-20-03-C | Work and Reimbursement | Right of Way        | 1,000,000.00                      | -                                  | ---                         | ---                          | PO/PA/PRR          |
| Sossaman Road: Ray to Warner Rd                              | ACI-SOS-20-03   | Work and Reimbursement | Construction        | 4,704,364.94                      | 557,127.83                         | Completed 8/2021            | Completed 11/2021            | PRR                |
| Mesa Main Street: Mesa Dr to Gilbert Rd Light Rail Extension | ACI-LRT-10-03   | Reimbursement Only     | N/A                 | 943,400.00                        | -                                  | N/A                         | N/A                          | ---                |
| Mountain Rd: SR24 to Pecos Rd                                | ACI-MOU-10-03   | Work and Reimbursement | Construction        | 9,487,721.63                      | -                                  | Completed 11/2023           | Completed 4/2026             | PRR                |
| <b>PEORIA</b>                                                |                 |                        |                     |                                   |                                    |                             |                              |                    |
| El Mirage Rd: L303 to Jomax (ADOT Administered)              | ACI-ELM-40-03   | Work and Reimbursement | Right of Way        | 25,371,361.03                     | -                                  | Completed 4/2026            | ---                          | PA/PRR             |
| <b>PHOENIX</b>                                               |                 |                        |                     |                                   |                                    |                             |                              |                    |
| Happy Valley Rd: 35th Ave to 67th Ave                        | ACI-HPV-20-03-B | Work and Reimbursement | Right of Way        | 155,649.06                        | -                                  | Completed 9/2021            | Completed 12/2021            | PRR                |
| Happy Valley Rd: 35th Ave to 67th Ave                        | ACI-HPV-20-03-B | Work and Reimbursement | Construction        | Funds obligated in FFY 24         | -                                  | Completed 9/2021            | Completed 12/2021            | PRR                |
| <b>SCOTTSDALE/CAREFREE</b>                                   |                 |                        |                     |                                   |                                    |                             |                              |                    |
| Happy Valley Rd: Pima Rd to Alma School Rd (SCT)             | ACI-PMA-10-03-B | Work and Reimbursement | Construction        | 682,780.54                        | 682,780.54                         | Completed 12/2017           | Completed 2/2018             | ---                |
| Pima Rd: Pinnacle Peak to Happy Valley Rd (SCT)              | ACI-PMA-10-03-C | Work and Reimbursement | Construction        | 239,871.10                        | 239,871.10                         | Completed 4/2016            | Completed 7/2016             | PRR                |
| Pima Rd: Dynamite Blvd to Las Piedras (SCT)                  | ACI-PMA-10-03-D | Work and Reimbursement | Construction        | 17,889,091.16                     | 75,751.77                          | Completed 8/2021            | Completed 4/2022             | PRR                |

| Facility/Location                                | RTP ID          | FY 26<br>Programming   | FY 26 Work<br>Phase | FY 26 Programmed<br>Reimbursement | FY Reimbursed<br>through 6/30/2026 | Project<br>Overview<br>(PO) | Project<br>Agreement<br>(PA) | Needed in<br>FY 26 |
|--------------------------------------------------|-----------------|------------------------|---------------------|-----------------------------------|------------------------------------|-----------------------------|------------------------------|--------------------|
| <b>SCOTTSDALE/CAREFREE (Cont.)</b>               |                 |                        |                     |                                   |                                    |                             |                              |                    |
| Pima Rd: Las Piedras to Stagecoach Pass Rd (SCT) | ACI-PMA-10-03-G | Work and Reimbursement | Construction        | 23,554,157.68                     | -                                  | Completed 6/2026            | ---                          | PA/PRR             |
| Pima Rd: Stagecoach Pass Rd to Cave Creek (CFR)  | ACI-PMA-10-03-E | Work and Reimbursement | Construction        | 5,250,855.40                      | -                                  | Completed 6/2026            | ---                          | PA/PRR             |
| <b>SCOTTSDALE</b>                                |                 |                        |                     |                                   |                                    |                             |                              |                    |
| Carefree Hwy: Cave Creek Rd to Scottsdale Rd     | ACI-CFR-10-03   | Work and Reimbursement | Construction        | 21,666,641.96                     | 248,918.72                         | Completed 7/2022            | Completed 12/2022            | PRR                |
| Miller Rd/SR-101L Underpass (Phase II)           | ACI-MLR-10-03-B | Work and Reimbursement | Right of Way        | 897,791.00                        | -                                  | ---                         | ---                          | ---                |
| Pima Rd: Happy Valley Rd to Jomax Rd             | ACI-PMA-20-03-A | Work and Reimbursement | Construction        | 11,682,481.39                     | 225,184.29                         | Completed 10/2021           | Completed 3/2022             | PRR                |
| Pima Rd: Jomax Rd to Dynamite Blvd               | ACI-PMA-20-03-C | Work and Reimbursement | Design              | 210,000.00                        | -                                  | Completed 6/2026            | ---                          | PA/PRR             |
| Pima Rd: Via Linda to Via de Ventura             | ACI-PMA-30-03-A | Work and Reimbursement | Construction        | 22,012,410.89                     | -                                  | Completed 9/2014            | Completed 12/2014            | PRR                |
| Raintree Drive: Scottsdale Rd to Hayden Rd       | ACI-SAT-10-03-F | Work and Reimbursement | Construction        | 943,153.33                        | 852,265.82                         | Completed 8/2014            | Completed 12/2014            | PRR                |
| Raintree Dr: Hayden Rd to Loop 101               | ACI-SAT-10-03-G | Work and Reimbursement | Right of Way        | 304,688.51                        | 1,800.38                           | Completed 10/2017           | Completed 2/2018             | PRR                |
| Scottsdale Rd: Pinnacle Peak Pkwy to Jomax Rd    | ACI-SCT-10-03-C | Work and Reimbursement | Design              | 210,000.00                        | -                                  |                             |                              | PO/PA/PRR          |
| Scottsdale Rd: Jomax Rd to Dixileta Dr           | ACI-SCT-20-03-A | Work and Reimbursement | Construction        | 29,798,680.38                     | 149,859.25                         | Completed 9/2014            | Completed 12/2014            | PRR                |
| Scottsdale Rd: Dixileta Dr to Carefree Hwy       | ACI-SCT-20-03-B | Work and Reimbursement | Right of Way        | 26,508,922.12                     | -                                  | Completed 5/2024            | ---                          | PA/PRR             |

| Facility/Location                            | RTP ID          | FY 26<br>Programming   | FY 26 Work<br>Phase | FY 26 Programmed<br>Reimbursement | FY Reimbursed<br>through 6/30/2026 | Project<br>Overview<br>(PO) | Project<br>Agreement<br>(PA) | Needed in<br>FY 26 |
|----------------------------------------------|-----------------|------------------------|---------------------|-----------------------------------|------------------------------------|-----------------------------|------------------------------|--------------------|
| <b>SCOTTSDALE (Cont.)</b>                    |                 |                        |                     |                                   |                                    |                             |                              |                    |
| Shea Blvd Intersection Improvements          | ACI-SHA-20-03-D | Work and Reimbursement | Construction        | 3,576,478.40                      | 2,148,179.32                       | Completed 9/2014            | Completed 12/2014            | PRR                |
| Hualapai Dr: 83rd St to Pima Rd              | ACI-UNH-10-03-D | Work and Reimbursement | Right of Way        | 715,427.33                        | -                                  | ---                         | ---                          | ---                |
| Hayden/Miller: Pinnacle Peak to Happy Valley | ACI-HAY-10-03   | Work and Reimbursement | Construction        | 819,216.20                        | 760,207.88                         | Completed 2/2021            | Completed 10/2021            | PRR                |

**Table 4.1: Status of RARF Funded Projects Underway in FY 2026**

| Facility/Location                                                    | RTP ID          | Work (W) and/or Reimb. (R) in FY26 | Reimbursements            |                  |                  |                        | Unfunded FY27+ (2024\$) | Expenditures                    |                  |                        |                              | Final FY for Const | Length* (Miles) | Other Project Information |
|----------------------------------------------------------------------|-----------------|------------------------------------|---------------------------|------------------|------------------|------------------------|-------------------------|---------------------------------|------------------|------------------------|------------------------------|--------------------|-----------------|---------------------------|
|                                                                      |                 |                                    | Total reimb. through FY25 | Act. Reimb. FY26 | Est. Reimb. FY27 | Total Reimb. FY06-FY27 |                         | Total Exp. through FY25 (YOE\$) | Actual Exp. FY26 | Est. Exp. FY27 (YOE\$) | Total Exp. FY06-FY27 (YOE\$) |                    |                 |                           |
| FOUNTAIN HILLS                                                       |                 |                                    |                           |                  |                  |                        |                         |                                 |                  |                        |                              |                    |                 |                           |
| Shea Blvd: Palisades Blvd to Technology Dr                           | ACI-SHA-10-03-C | W/R                                | 0.244                     | 0.591            | 1.690            | 2.525                  | 0.339                   | 0.348                           | 0.844            | 2.290                  | 3.483                        | 2025               | 2.20            |                           |
| GILBERT                                                              |                 |                                    |                           |                  |                  |                        |                         |                                 |                  |                        |                              |                    |                 |                           |
| Elliot Rd at Cooper Rd: Intersection Improvements                    | AII-ELT-30-03   | R                                  | 3.919                     | 0.000            | 4.329            | 8.248                  | 0.000                   | 5.598                           | 0.000            | 5.521                  | 11.119                       | 2026               | 0.50            |                           |
| McQueen Rd at Elliot Rd                                              | AII-MCQ-30-03   | R                                  | 0.426                     | 1.187            | 5.137            | 6.750                  | 1.814                   | 0.608                           | 1.696            | 14.110                 | 16.414                       | 2026               | 0.50            |                           |
| McQueen Rd at Guadalupe Rd                                           | AII-MCQ-40-03   | R                                  | 0.000                     | 0.000            | 6.844            | 6.844                  | 0.000                   | 0.000                           | 0.000            | 15.806                 | 15.806                       | 2026               | 0.50            |                           |
| GILBERT/MARICOPA COUNTY/MESA/QUEEN CREEK                             |                 |                                    |                           |                  |                  |                        |                         |                                 |                  |                        |                              |                    |                 |                           |
| Power Rd: East Maricopa Floodway to Santan Fwy/Loop 202 (Pre-design) | ACI-PWR-20-03-A | W/R                                | 0.451                     | 0.377            | 7.365            | 8.193                  | 0.000                   | 0.894                           | 0.538            | 29.529                 | 30.961                       | 2026               | 3.50            |                           |
| MARICOPA COUNTY                                                      |                 |                                    |                           |                  |                  |                        |                         |                                 |                  |                        |                              |                    |                 |                           |
| Gilbert Rd: Bridge over the Salt River                               | ACI-GIL-20-03   | R                                  | 40.105                    | 0.867            | 0.000            | 40.973                 | 0.000                   | 57.293                          | 1.239            | 0.000                  | 58.532                       | 2025               | 1.60            |                           |
| McKellips Rd: Loop 101 to SRP-MIC/Alma School Rd                     | ACI-MCK-40-03   | R                                  | 4.803                     | 9.453            | 0.000            | 14.256                 | 14.567                  | 6.861                           | 13.504           | 0.000                  | 20.365                       | 2025               | 2.00            |                           |
| MESA                                                                 |                 |                                    |                           |                  |                  |                        |                         |                                 |                  |                        |                              |                    |                 |                           |
| Broadway Rd: Country Club Dr to Mesa Dr                              | ACI-BDW-20-03-A | W/R                                | 0.000                     | 0.000            | 1.091            | 1.091                  | 0.000                   | 0.000                           | 0.000            | 18.927                 | 18.927                       | 2023               | 1.00            |                           |

| MESA (Cont.)                                                    |                 |     |        |       |        |        |       |        |       |        |        |      |      |                                                                      |
|-----------------------------------------------------------------|-----------------|-----|--------|-------|--------|--------|-------|--------|-------|--------|--------|------|------|----------------------------------------------------------------------|
| Broadway Rd:<br>Mesa Dr to<br>Stapley Dr                        | ACI-BDW-20-03-B | W/R | 2.288  | 1.305 | 43.995 | 47.588 | 0.000 | 3.269  | 1.865 | 63.572 | 68.705 | 2023 | 1.00 |                                                                      |
| Country Club Dr:<br>US 60 to<br>Southern Ave                    | ACI-CCB-20-03   | W/R | 0.000  | 0.000 | 7.986  | 7.986  | 0.000 | 0.000  | 0.000 | 11.408 | 11.408 | 2027 | 0.50 |                                                                      |
| Mesa Dr: US 60<br>to Southern Ave                               | ACI-MES-10-03-A | R   | 16.547 | 0.000 | 0.036  | 16.584 | 0.000 | 23.881 | 0.000 | 0.052  | 23.933 | 2017 | 1.00 |                                                                      |
| Mesa Dr: 8th<br>Avenue to Main<br>Street                        | ACI-MES-10-03-B | W/R | 13.116 | 0.000 | 0.527  | 13.643 | 0.000 | 23.961 | 0.000 | 0.861  | 24.822 | 2023 | 1.00 |                                                                      |
| Signal Butte Rd:<br>Williams Field Rd<br>to Germann Rd          | ACI-SGB-10-03-C | W/R | 3.883  | 0.000 | 2.579  | 6.462  | 0.000 | 5.547  | 0.000 | 3.684  | 9.231  | 2022 | 2.00 | Design and<br>ROW phase<br>only,<br>Construction<br>STBGP<br>funded. |
| Southern Ave at<br>Stapley Dr:<br>Intersection<br>Improvements  | ACI-SOU-10-03-B | R   | 3.553  | 0.000 | 1.296  | 4.849  | 0.000 | 19.234 | 0.000 | 1.930  | 21.164 | 2022 | 1.00 | Construction<br>also funded<br>by<br>HSIP/STBGP                      |
| Stapley Dr at<br>University Dr:<br>Intersection<br>Improvements | All-STA-10-03   | R   | 0.600  | 0.000 | 1.552  | 2.152  | 0.000 | 0.857  | 0.000 | 20.504 | 21.361 | 2026 | 0.50 |                                                                      |
| Val Vista Dr: US-<br>60 to Pueblo                               | ACI-VAL-10-03-C | W/R | 1.171  | 1.584 | 10.443 | 13.198 | 3.901 | 1.673  | 2.263 | 12.848 | 16.784 | 2026 | 1.50 |                                                                      |
| Ray Road: SR 24<br>to Ellsworth Rd                              | ACI-RAY-30-03   | W/R | 1.161  | 4.778 | 3.231  | 9.170  | 0.000 | 1.659  | 6.826 | 4.653  | 13.138 | 2025 | 1.00 |                                                                      |
| Ellsworth Rd and<br>Williams Field Rd<br>Bridge                 | ACI-ELL-20-03-A | W/R | 5.717  | 0.000 | 1.064  | 6.781  | 0.000 | 8.167  | 0.000 | 1.949  | 10.116 | 2025 | 3.00 |                                                                      |
| Ellsworth Rd:<br>Germann Rd to<br>Ray Rd                        | ACI-ELL-20-03-B | W/R | 1.390  | 2.972 | 20.974 | 25.336 | 0.000 | 1.986  | 4.246 | 26.199 | 32.430 | 2025 | 3.00 |                                                                      |
| Williams Field Rd:<br>SR24 to Ellsworth                         | ACI-ELL-20-03-C | W/R | 0.000  | 0.000 | 1.000  | 1.000  | 0.000 | 0.000  | 0.000 | 4.695  | 4.695  | 2025 | 3.00 |                                                                      |
| Sossaman Rd:<br>Ray Rd to Warner<br>Rd                          | ACI-SOS-20-03   | W/R | 3.644  | 0.557 | 4.147  | 8.348  | 0.000 | 5.205  | 0.796 | 10.609 | 16.610 | 2025 | 1.00 |                                                                      |

| MESA (Cont.)                                       |                 |     |        |       |        |        |       |        |       |        |        |      |      |                                                  |
|----------------------------------------------------|-----------------|-----|--------|-------|--------|--------|-------|--------|-------|--------|--------|------|------|--------------------------------------------------|
| Mountain Rd:<br>SR24 to Pecos Rd                   | ACI-MOU-10-03   | W/R | 0.000  | 0.000 | 9.488  | 9.488  | 0.431 | 0.000  | 0.000 | 16.684 | 16.684 | 2026 | 1.50 |                                                  |
| PHOENIX                                            |                 |     |        |       |        |        |       |        |       |        |        |      |      |                                                  |
| Happy Valley Rd:<br>35th Ave to 67th Ave           | ACI-HPV-20-03-B | W/R | 1.419  | 0.000 | 0.156  | 1.575  | 0.000 | 1.786  | 0.000 | 0.469  | 2.255  | 2027 | 4.00 | Design/ROW phase only, Construction STBGP funded |
| SCOTTSDALE/CAREFREE                                |                 |     |        |       |        |        |       |        |       |        |        |      |      |                                                  |
| Happy Valley Rd:<br>Pima Rd to Alma School Rd      | ACI-PMA-10-03-B | W/R | 20.598 | 0.683 | 0.000  | 21.280 | 0.000 | 29.425 | 0.975 | 0.000  | 30.401 | 2025 | 2.00 |                                                  |
| Pima Rd: Pinnacle Peak to Happy Valley Rd          | ACI-PMA-10-03-C | W/R | 19.694 | 0.240 | 0.175  | 20.109 | 0.000 | 28.134 | 0.343 | 1.247  | 29.723 | 2025 | 1.00 |                                                  |
| Pima Rd:<br>Dynamite Blvd to Las Piedras           | ACI-PMA-10-03-D | W/R | 0.567  | 0.076 | 17.813 | 18.456 | 0.000 | 0.810  | 0.108 | 25.629 | 26.548 | 2026 | 1.30 |                                                  |
| Pima Rd: Las Piedras to Stagecoach Rd (SCT)        | ACI-PMA-10-03-G | W/R | 0.000  | 0.000 | 23.554 | 23.554 | 0.000 | 0.000  | 0.000 | 33.649 | 33.649 | 2026 | 3.70 |                                                  |
| Pima Rd:<br>Stagecoach Pass Rd to Cave Creek (CFR) | ACI-PMA-10-03-E | W/R | 0.000  | 0.000 | 5.251  | 5.251  | 0.307 | 0.000  | 0.000 | 7.940  | 7.940  | 2026 | 0.25 |                                                  |
| SCOTTSDALE                                         |                 |     |        |       |        |        |       |        |       |        |        |      |      |                                                  |
| Carefree Hwy:<br>Cave Creek Rd to Scottsdale Rd    | ACI-CFR-10-03   | W/R | 1.203  | 0.249 | 0.508  | 1.960  | 0.000 | 1.719  | 0.356 | 0.647  | 2.721  | 2026 | 2.00 | Design/ROW phase only, Construction STBGP funded |
| Miller Rd/SR-101L Underpass (Phase II)             | ACI-MLR-10-03-B | W/R | 0.000  | 0.000 | 0.898  | 0.898  | 0.000 | 0.000  | 0.000 | 1.283  | 1.283  | -    | 0.25 |                                                  |
| Pima Rd: Happy Valley Rd to Jomax Rd               | ACI-PMA-20-03-A | W/R | 0.772  | 0.225 | 0.353  | 1.350  | 0.000 | 0.473  | 0.322 | 0.731  | 1.929  | 2026 | 1.00 | Design/ROW phase only, Construction STBGP funded |
| Pima Rd: Via Linda to McDowell Rd                  | ACI-PMA-30-03-A | W/R | 0.101  | 0.000 | 22.012 | 22.114 | 0.000 | 0.158  | 0.000 | 65.134 | 65.293 | 2026 | 7.20 | SRP-MIC Gran                                     |

| SCOTTSDALE (Cont.)                                     |                     |     |        |       |        |        |       |        |       |       |        |      |      |                                                                   |
|--------------------------------------------------------|---------------------|-----|--------|-------|--------|--------|-------|--------|-------|-------|--------|------|------|-------------------------------------------------------------------|
| Raintree Drive:<br>Scottsdale Rd to<br>Hayden Rd       | ACI-SAT-10-03-<br>F | W/R | 27.238 | 0.852 | 0.091  | 28.181 | 0.000 | 38.911 | 1.218 | 4.538 | 44.667 | 2025 | 1.20 |                                                                   |
| Raintree Dr:<br>Hayden Rd to<br>Loop 101               | ACI-SAT-10-03-<br>G | W/R | 1.588  | 0.002 | 0.303  | 1.892  | 0.000 | 2.268  | 0.003 | 4.479 | 6.750  | 2025 | 1.00 |                                                                   |
| Scottsdale Rd:<br>Pinnacle<br>Peak Pkwy to<br>Jomax Rd | ACI-SCT-10-03-<br>C | W/R | 0.000  | 0.000 | 0.210  | 0.210  | 0.000 | 0.000  | 0.000 | 0.300 | 0.300  | 2026 | 2.00 |                                                                   |
| Scottsdale Rd:<br>Jomax Rd to<br>Dixileta Dr           | ACI-SCT-20-03-<br>A | W/R | 3.620  | 0.150 | 29.649 | 33.419 | 0.000 | 5.171  | 0.214 | 0.514 | 5.900  | 2025 | 2.00 | Design/ROW<br>phase only,<br>Construction<br>HSIP/STBGP<br>funded |
| Shea Blvd<br>Intersection<br>Improvements              | ACI-SHA-20-03-<br>D | W/R | 2.902  | 2.148 | 1.428  | 6.479  | 0.000 | 4.146  | 3.069 | 2.040 | 9.256  | 2025 | 6.00 |                                                                   |
| Hualapai Dr: 83rd<br>St to Pima Rd                     | ACI-UNH-10-<br>03-D | W/R | 0.000  | 0.000 | 0.715  | 0.715  | 0.000 | 0.000  | 0.000 | 1.442 | 1.442  | -    | 0.50 | Design/ROW<br>only,<br>Construction<br>STBGP<br>funded            |
| Hayden/Miller:<br>Pinnacle Peak to<br>Happy Valley     | ACI-HAY-10-03       | W/R | 13.478 | 0.760 | 0.059  | 14.297 | 6.167 | 19.254 | 1.086 | 0.084 | 20.424 | 2025 | 1.00 |                                                                   |

**Table 4.2: Status of Federally-Funded Projects Underway in FY 2026**

| Facility/Location                                       | RTP ID          | Work (W) and/or Reimb. (R) in FY26 | Obligations        |             |                |                 | Unfunded FY27+ (2024\$) | Expenditures       |             |                |                 | Final FY for Const | Length* (Miles) | Other Project Information                              |
|---------------------------------------------------------|-----------------|------------------------------------|--------------------|-------------|----------------|-----------------|-------------------------|--------------------|-------------|----------------|-----------------|--------------------|-----------------|--------------------------------------------------------|
|                                                         |                 |                                    | Total through FY25 | Actual FY26 | Estimated FY26 | Total FY06-FY26 |                         | Total through FY25 | Actual FY26 | Estimated FY26 | Total FY06-FY26 |                    |                 |                                                        |
| CHANDLER                                                |                 |                                    |                    |             |                |                 |                         |                    |             |                |                 |                    |                 |                                                        |
| Chandler Heights Rd: Gilbert Rd to Val Vista Rd         | ACI-PRC-10-03-K | W/R                                | 8.899              | 0.000       | 0.000          | 8.899           | 0.000                   | 6.361              | 8.749       | 0.000          | 15.110          | 2026               | 2.00            |                                                        |
| Ocotillo Rd: Gilbert Rd to 148th Street                 | ACI-OCT-10-03   | R                                  | 3.178              | 0.000       | 0.000          | 3.178           | 0.000                   | 6.086              | 0.000       | 0.000          | 6.086           | 2024               | 1.50            | Awaiting closeout                                      |
| Lindsay Road: Ocotillo Rd to Hunt Hwy                   | ACI-LND-10-03   | W/R                                | 17.569             | 0.000       | 0.000          | 17.569          | 0.000                   | 8.781              | 1.152       | 24.765         | 34.698          | 2026               | 3.00            |                                                        |
| GILBERT                                                 |                 |                                    |                    |             |                |                 |                         |                    |             |                |                 |                    |                 |                                                        |
| Warner Road: Recker Rd to Power Rd                      | ACI-WRN-20-03   | R                                  | 0.000              | 0.000       | 10.417         | 10.417          | 8.093                   | 0.000              | 0.000       | 14.881         | 14.881          | 2025               | 1.00            |                                                        |
| MARICOPA COUNTY                                         |                 |                                    |                    |             |                |                 |                         |                    |             |                |                 |                    |                 |                                                        |
| McKellips Rd: Loop 101 to SRP-MIC/Alma School Rd        | ACI-MCK-40-03   | R                                  | 0.294              | 0.000       | 0.000          | 0.294           | 0.000                   | 0.421              | 0.000       | 0.000          | 0.421           | 2025               | 2.00            | Pre-Design only, Design, ROW, Construction RARF funded |
| Main St: Sossaman Rd to Meridian Rd (ADOT Administered) | ACI-MAN-10-03   | W/R                                | 14.005             | 0.000       | 0.000          | 14.005          | 0.000                   | 19.127             | 0.043       | 1.782          | 20.951          | 2026               | 5.00            | Project is administered by ADOT                        |

| MARICOPA COUNTY (Cont.)                                               |                 |     |         |        |        |         |       |         |       |        |         |      |      |                                                     |
|-----------------------------------------------------------------------|-----------------|-----|---------|--------|--------|---------|-------|---------|-------|--------|---------|------|------|-----------------------------------------------------|
| Northern Parkway:<br>Dysart to 111th Ave                              | ACI-NOR-10-03-B | R   | 54.718  | 0.000  | 0.000  | 54.718  | 0.000 | 72.562  | 0.000 | 0.000  | 72.562  | 2021 | 2.50 | Closed - Oct 2025                                   |
| Northern Parkway:<br>103rd to 91st Ave                                | ACI-NOR-10-03-D | W/R | 9.304   | 0.000  | 46.020 | 55.323  | 0.000 | 6.882   | 2.569 | 83.970 | 93.421  | 2025 | 1.50 | Reauthorization underway                            |
| Northern Parkway:<br>El Mirage<br>Alternative Access                  | ACI-NOR-20-03-A | W/R | 5.815   | 0.000  | 0.000  | 5.815   | 0.000 | 7.382   | 0.000 | 0.000  | 7.382   | 2023 | 1.00 | Closed - Dec 2025                                   |
| Northern Parkway:<br>Agua Fria to 103th<br>Ave                        | ACI-NOR-20-03-C | W/R | 22.008  | 0.000  | 0.000  | 22.008  | 0.000 | 4.671   | 0.230 | 27.197 | 32.099  | 2026 | 3.00 |                                                     |
| MESA                                                                  |                 |     |         |        |        |         |       |         |       |        |         |      |      |                                                     |
| Elliot Rd: Eastern<br>Maricopa Floodway<br>(EMF) to Ellsworth         | ACI-ELT-10-03-F | W/R | 1.911   | 22.510 | 0.000  | 24.421  | 0.000 | 1.578   | 1.083 | 32.226 | 34.887  | 2026 | 2.60 |                                                     |
| SR 24 Arterial<br>Improvements                                        | ACI-ELL-10-03-A | R   | 0.658   | 0.000  | 0.811  | 1.469   | 0.000 | 0.941   | 0.000 | 0.000  | 0.941   | 2023 | 3.00 | Amount programmed in FY 26<br>is savings only       |
| Signal Butte Rd:<br>Williams Field Rd to<br>Germann Rd                | ACI-SGB-10-03-C | W/R | 9.214   | 0.000  | 3.171  | 12.385  | 0.000 | 13.163  | 0.000 | 4.530  | 17.693  | 2023 | 1.00 | Amount programmed in FY 26<br>is savings only       |
| Southern Ave at<br>Stapley Dr:<br>Intersection<br>Improvements        | ACI-SOU-10-03-B | W/R | 10.218  | 0.000  | 0.000  | 10.218  | 0.000 | 13.751  | 0.000 | 0.000  | 13.751  | 2023 | 1.00 | Partial Const only,<br>Design/ROW/Const RARF funded |
| Mesa Main Street:<br>Mesa Dr to Gilbert<br>Rd Light Rail<br>Extension | ACI-LRT-10-03   | R   | 169.687 | 0.000  | 0.943  | 170.631 | 0.000 | 242.410 | 0.000 | 1.348  | 243.758 | 2023 | 1.00 | Partial Const only,<br>Design/ROW/Const RARF funded |

| PEORIA                                                                                    |                 |     |        |        |        |        |       |       |       |        |        |      |      |                                                    |
|-------------------------------------------------------------------------------------------|-----------------|-----|--------|--------|--------|--------|-------|-------|-------|--------|--------|------|------|----------------------------------------------------|
| El Mirage Rd: L303 to Jomax (ADOT Administered)                                           | ACI-ELM-40-03   | W/R | 1.000  | 16.231 | 9.140  | 26.371 | 0.000 | 1.429 | 0.000 | 36.429 | 37.858 | 2027 | 1.60 | Project is administered by ADOT.                   |
| PHOENIX                                                                                   |                 |     |        |        |        |        |       |       |       |        |        |      |      |                                                    |
| Happy Valley Rd: 35th Ave to 67th Ave                                                     | ACI-HPV-20-03-B | W/R | 14.142 | 0.000  | 0.000  | 14.142 | 0.000 | 0.000 | 0.000 | 32.453 | 32.453 | 2027 | 4.00 | Construction phase only, Design/ROW RARF funded.   |
| SCOTTSDALE                                                                                |                 |     |        |        |        |        |       |       |       |        |        |      |      |                                                    |
| Carefree Hwy: Cave Creek Rd to Scottsdale Rd                                              | ACI-CFR-10-03   | W/R | 0.000  | 0.000  | 20.910 | 20.910 | 0.000 | 0.000 | 0.000 | 29.871 | 29.871 | 2026 | 1.00 | Construction only, Design/ROW RARF funded          |
| Pima Rd: Happy Valley Rd to Jomax Rd                                                      | ACI-PMA-20-03-A | W/R | 0.000  | 0.000  | 11.282 | 11.282 | 0.000 | 0.000 | 0.000 | 16.779 | 16.779 | 2026 | 1.00 | Construction only, Design/ROW RARF funded          |
| Pima Rd: Jomax Rd to Dynamite Blvd                                                        | ACI-PMA-20-03-C | W/R | 0.000  | 0.000  | 0.210  | 0.210  | 0.000 | 0.000 | 0.000 | 0.300  | 0.300  | 2026 | 1.00 | Construction only, Design/ROW RARF funded          |
| Scottsdale Rd: Dixileta Dr to Carefree Hwy                                                | ACI-SCT-20-03-B | W/R | 0.000  | 0.000  | 26.509 | 26.509 | 0.000 | 0.000 | 0.000 | 40.138 | 40.138 | 2026 | 1.00 |                                                    |
| Hualapai Dr: 83rd St to Pima Rd                                                           | ACI-UNH-10-03-D | W/R | 0.294  | 0.000  | 0.000  | 0.294  | 0.000 | 0.000 | 0.000 | 0.420  | 0.420  | 2026 | 0.50 | Construction only, Design/ROW RARF funded          |
| Loop 101 Traffic Interchanges: Frank Lloyd Wright, Raintree, and Shea (ADOT Administered) | ACI-LOP-10-03   | W/R | 5.864  | 0.000  | 0.000  | 5.864  | 0.000 | 8.785 | 0.000 | 0.000  | 8.785  | 2025 | 0.80 | Construction only, Project is administered by ADOT |
